





FAST DANUBE 2

Improvement of Navigation Conditions on the Romanian-Bulgarian Common Sector of the Danube

Co-financed by the European Union
Connecting Europe Facility

FAST DANUBE 2

12.11.2026, Budapest

General information

Co-funded by the European Union

Project name:

Improvement of Navigation Conditions on the Romanian Bulgarian Common Sector of the Danube

Acronym: **FAST Danube 2**

Project partners:

Romania: 

- River Administration of the Lower Danube Galati – AFDJ Galati - Lead partner

Bulgaria: 

- Executive Agency for exploration and maintenance of the Danube river - EAEMDR Ruse - Partner;
- Ministry of Transport and Communications - Affiliated partner.

Co-funded by the European Union. Views and opinions expressed are however those of the author(s) only and do not necessarily reflect those of the European Union or the European Climate, Infrastructure and Environment Executive Agency (CINEA).
Neither the European Union nor CINEA can be held responsible for them.

FAST DANUBE 2

- ***Joint procurement procedure and signing the Environmental Monitoring Contract***

The procurement procedure was carried out by AFDJ, as the procurement leader.

The Agreement for joint procurement was signed by both project partners in 24.04.2025.

The contract was signed in 19.08.2026

The Monitoring Plan was received in 18.09.2026





Co-financed by the European Union
Connecting Europe Facility

Overview Timeline - Procurement for environmental monitoring

Contract duration - 108 months (August 2026 - August 2035)
In accordance with the environmental permits issued in Romania and Republic of Bulgaria, the environmental monitoring program will be carried out 9 years (108 months)

- 2 years before the start of the works *(08/2026 – 08/2028),*
- 2 years during the execution of the works *(08/2028 – 08/2030)*
- 5 years after the completion of the works, as follows:
  - *3 years for all environmental factors (08/2030 – 08/2033)*
  - and further *2 years of monitoring only for biodiversity factors (08/2033 – 08/2035)*

Co-financed by the European Union
Connecting Europe Facility

Overview Timeline - Procurement for Design & Works

➢ ***Organizing the Joint procurement procedure and signing the Design & Execution of Works Contract***

The procurement procedure is carried out by AFDJ, as the procurement leader.

The Agreement for joint procurement was signed by both project partners in 22.07.2025.

The offer opening 09.02.2026
Contract signing December 2026

Co-financed by the European Union
Connecting Europe Facility

Overview Timeline - Procurement for supervision

➢***Organizing the Joint procurement procedure and signing the Supervision of the Works Execution Contract***

The procurement procedure is carried out by AFDJ, as the procurement leader.


The Agreement for joint procurement was signed by both project partners in 22.07.2025.

The offers opening 06.04.2026

Contract signing December 2026

Co-financed by the European Union
Connecting Europe Facility



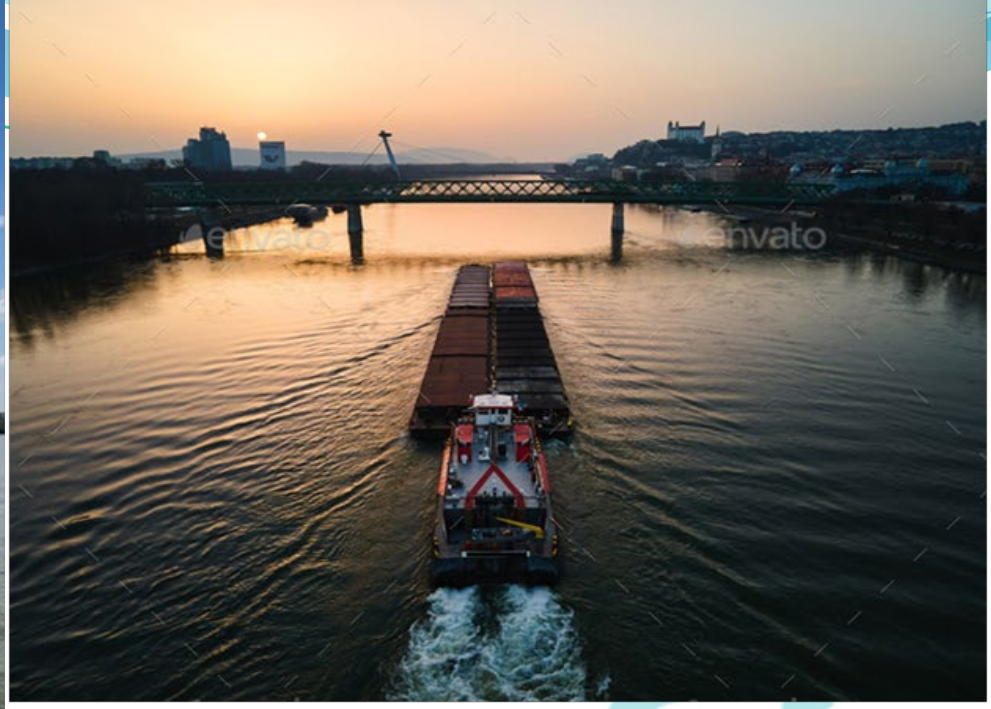

Thank you for your attention!

AFDJ Galati Team

IAPPD Ruse Team

EAEMDR Ruse

Co-financed by the European Union
Connecting Europe Facility
